DONEL KINNARD MEMORIAL STATE VETERANS CEM

(CONSTRUCTION PROGRESS SCHEDULE)

Date: 12/28/11

ID	Task Name	Duration	Start	Finish	Predecessors
1	Notice to Proceed	0 days	Tue 10/12/10	Tue 10/12/10	
2	Stake out limits	2 wks	Wed 10/20/10	Tue 11/2/10	
3	Clearing and Grubbing	6 wks	Wed 10/27/10	Thu 12/9/10	
4	**Temp Rd/Box Culverts**	**134 days**	**Wed 11/3/10**	**Fri 5/13/11**	
5	Temp Rd Areas 1-3	7 days	Wed 11/3/10	Thu 11/11/10	3SS+1 wk
6	Box Culvert Foundations Area 3-4	15 days	Fri 11/19/10	Mon 12/13/10	
7	Temp Rd Areas 4-7	14 days	Mon 11/22/10	Mon 12/13/10	5,6FF
8	Box Culvert Foundations Area 5-6	102 days	Tue 12/14/10	Fri 5/6/11	6,7
9	Set/Backfill All Box Culverts	25 days	Mon 4/11/11	Fri 5/13/11	8FF+5 days
10	Finalize Temp Rd	5 days	Fri 4/8/11	Thu 4/14/11	9
11	Rough Grading Area 3	1 wk	Wed 11/3/10	Tue 11/9/10	3SS+1 wk
12	Rough Grading Area 1 & 2	5 mons	Fri 11/12/10	Wed 4/6/11	11,5
13	Rough Grading Area 4-7	2.5 mons	Thu 1/27/11	Wed 4/6/11	
14	Roadway Stone Base	3 wks	Tue 6/7/11	Fri 9/16/11	64FF+1 wk
15	**Maintenance Bld & Storage Shed**	**308 days**	**Thu 11/11/10**	**Thu 1/26/12**	
16	Grade Bld Pad	0 wks	Thu 11/11/10	Thu 11/11/10	9SS+1 wk
17	Dig/Form Foundations	6 days	Fri 11/12/10	Fri 11/19/10	16
18	Underground Rough-Ins	20 days	Mon 11/22/10	Tue 12/21/10	17
19	Slab-On-Grade/Foundation	8 days	Wed 12/22/10	Tue 1/4/11	18
20	Pre-Engineered Metal Bld Structure	12 wks	Mon 2/21/11	Fri 5/13/11	19FS+1 wk
21	MEP Rough-Ins	4 wks	Mon 5/16/11	Mon 6/13/11	20
22	Set Windows	2 days	Mon 11/14/11	Tue 11/15/11	25FS+2 wks
23	Interior Finish Selection	0 days	Wed 9/7/11	Wed 9/7/11	
24	Interior Finishes	4 wks	Fri 12/30/11	Thu 1/26/12	23FF+2 wks,21,68
25	Masonry Veneer/Exterior Finishes	3 wks	Tue 9/20/11	Mon 10/10/11	41
26	Exterior Concrete Pads	1 wk	Mon 10/10/11	Fri 10/14/11	69
27	Set Fuel Tank	1 wk	Mon 10/17/11	Fri 10/21/11	26
28	Chain Link Fence	2 wks	Mon 1/9/12	Fri 1/20/12	26
29					
30	**Admin Building**	**307 days**	**Mon 11/22/10**	**Thu 2/2/12**	
31	Grade Bld Pad & Stone Parking	1 wk	Mon 11/22/10	Tue 11/30/10	17

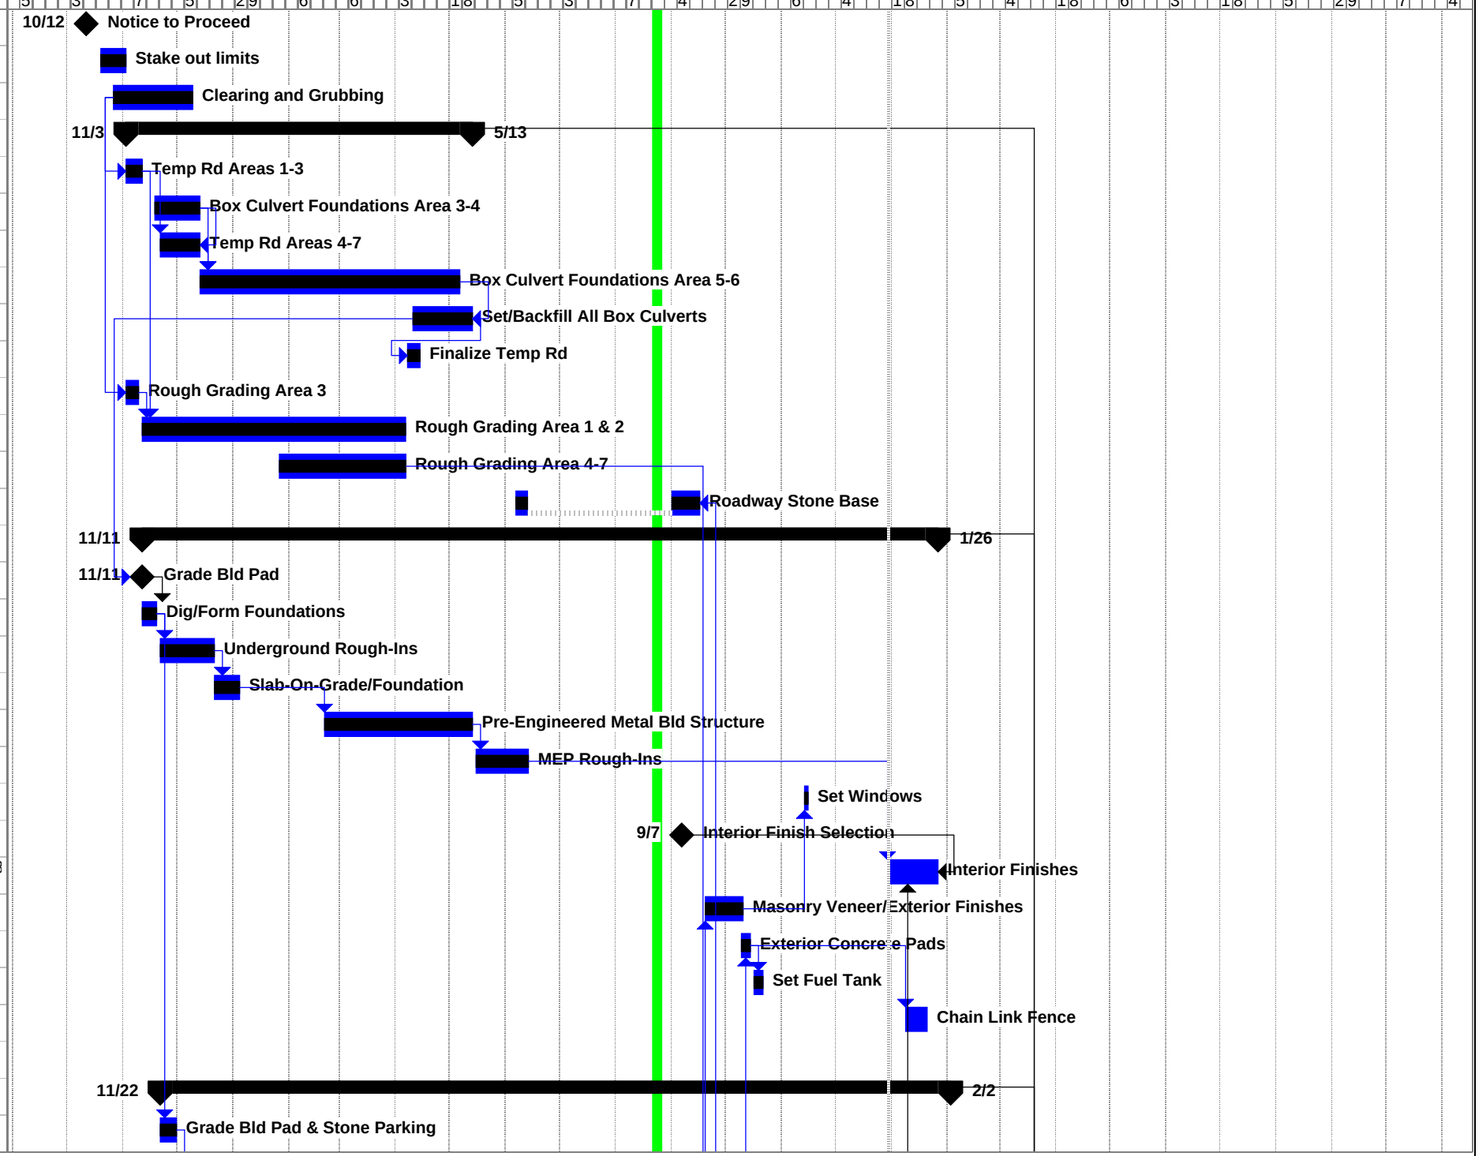

BBLCarlton
"The Way to Build Today!"
900 Lee Street, Suite 1400
Charleston, WV 25301
Phone 304.345.1300
Fax 304.345.1304
www.BBLCarlton.com
WV028886

Task — Milestone — Rolled Up Critical Task — Split — Group By Summary

Critical Task — Summary — Rolled Up Milestone — External Tasks — Deadline

Progress — Rolled Up Task — Rolled Up Progress — Project Summary

DONEL KINNARD MEMORIAL STATE VETERANS CEM

(CONSTRUCTION PROGRESS SCHEDULE)

Date: 12/28/11

ID	Task Name	Duration	Start	Finish	Predecessors
32	Dig/Form Foundations	25 days	Wed 12/1/10	Thu 1/6/11	31
33	Underground Rough-Ins	13 days	Fri 1/7/11	Tue 1/25/11	32
34	Slab-On-Grade/Foundation	23 days	Wed 1/26/11	Fri 2/25/11	33
35	Structural Steel	25 days	Mon 3/21/11	Fri 4/22/11	
36	Roof Framing & Sheathing	18 days	Mon 5/9/11	Thu 6/2/11	
37	Roof System and Accessories	15 days	Mon 8/15/11	Fri 9/2/11	
38	MEP Rough-Ins	4 wks	Mon 8/15/11	Mon 9/12/11	36,37FF+1 wk
39	Interior Finish Selection	0 days	Wed 9/7/11	Wed 9/7/11	
40	Interior Finishes	5 wks	Fri 12/30/11	Thu 2/2/12	38SS+2 wks,68
41	Masonry Veneer/Exterior Finishes	3 wks	Tue 8/23/11	Tue 9/13/11	
42					
43	**Committal Shelter/Columbariums**	**230 days**	**Thu 3/10/11**	**Mon 1/30/12**	
44	Grade Bld Pad	2 wks	Thu 3/10/11	Wed 3/23/11	
45	Dig/Pour Foundations	8 days	Thu 3/24/11	Mon 4/4/11	44
46	Structural Masonry	15 days	Mon 5/16/11	Mon 6/6/11	
47	Slab-On-Grade	4 days	Tue 6/7/11	Fri 6/10/11	46
48	Frame Roof Structure	15 days	Mon 6/13/11	Fri 7/1/11	47
49	Roof System and Accessories	10 days	Tue 9/6/11	Mon 9/19/11	37
50	Electrical Rough-Ins	4 days	Mon 8/8/11	Thu 8/11/11	49
51	Interior Finishes	2 wks	Fri 12/30/11	Thu 1/12/12	50,68
52	Masonry Veneer	4 wks	Tue 9/20/11	Mon 10/17/11	49
53	Decorative Concrete	4 wks	Tue 1/3/12	Mon 1/30/12	52
54	Set Columbarium Units	5 days	Mon 7/11/11	Fri 7/15/11	
55					
56	**Entry Wall**	**202 days**	**Mon 3/7/11**	**Fri 12/16/11**	
57	Foundations	10 days	Mon 3/7/11	Fri 3/18/11	
58	Utilities	5 days	Mon 5/16/11	Fri 5/20/11	59FF
59	Poured Walls	15 days	Mon 4/18/11	Fri 5/6/11	57
60	Masonry Veneer	10 days	Thu 11/10/11	Wed 11/23/11	52
61	Gates	10 days	Mon 12/5/11	Fri 12/16/11	60
62					

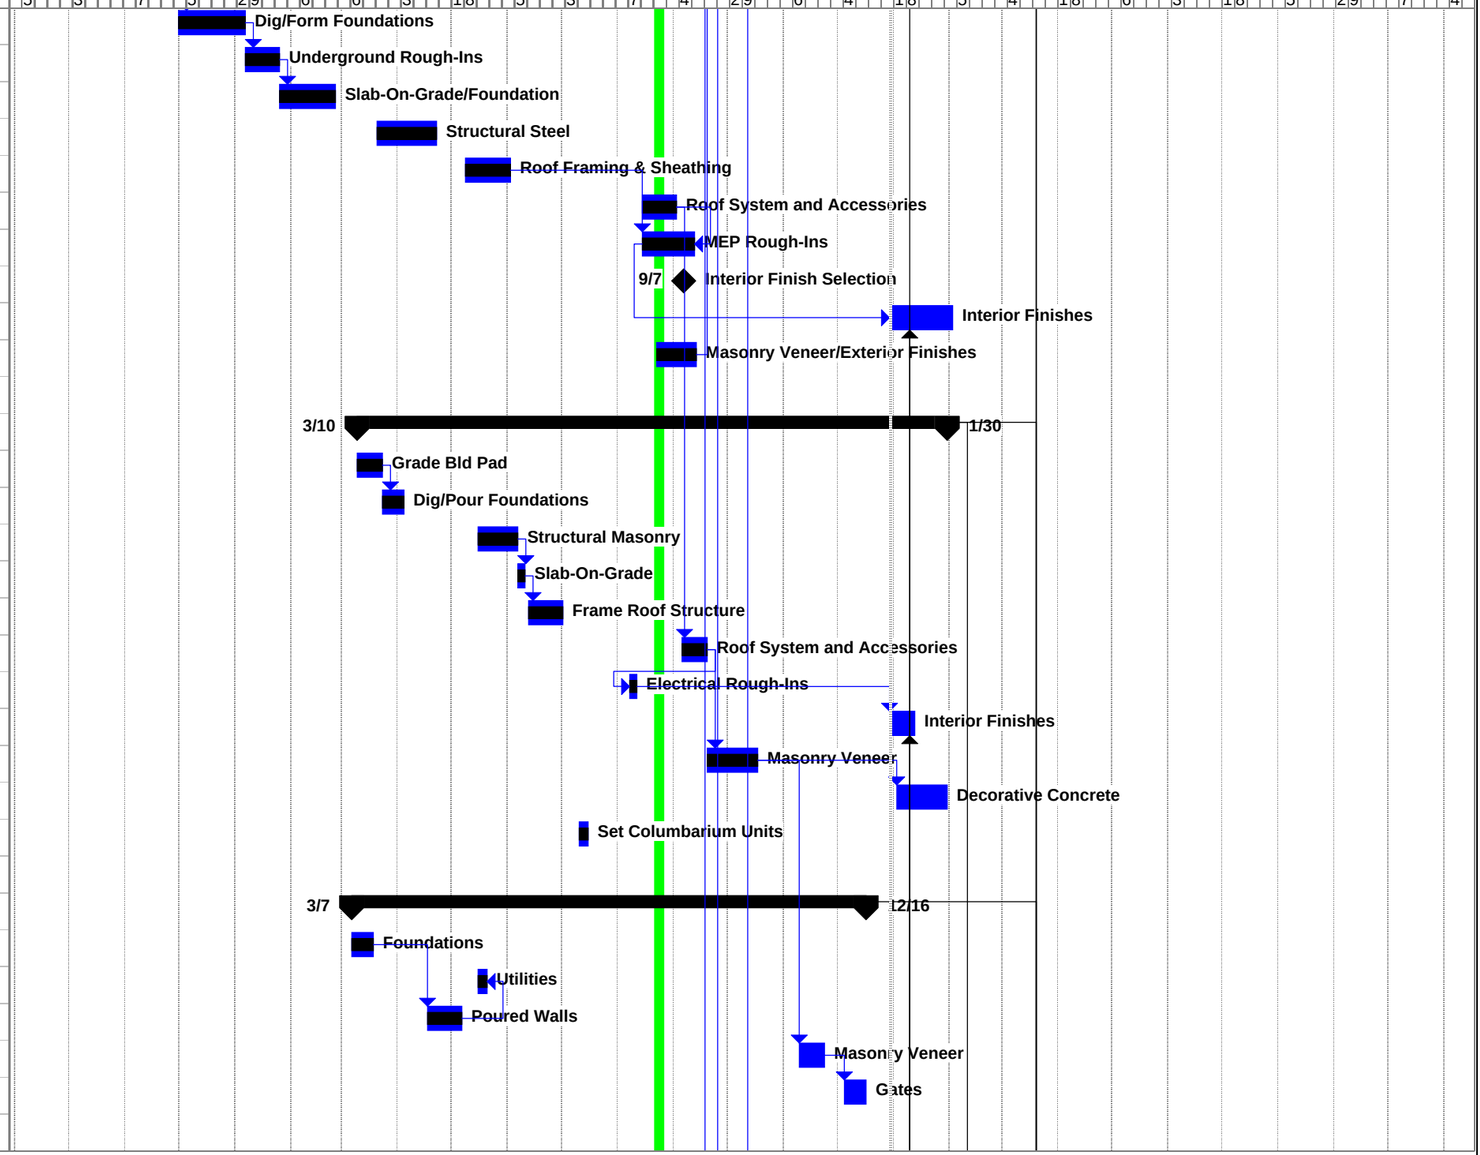

BBLCarlton
"The Way to Build Today!"
900 Lee Street, Suite 1400
Charleston, WV 25301
Phone 304.345.1300
Fax 304.345.1304
www.BBLCarlton.com
WV028886

Task	Milestone	Rolled Up Critical Task	Split		Group By Summary		
Critical Task	Summary	Rolled Up Milestone	External Tasks		Deadline		
Progress	Rolled Up Task	Rolled Up Progress	Project Summary				

DONEL KINNARD MEMORIAL STATE VETERANS CEM

(CONSTRUCTION PROGRESS SCHEDULE)

Date: 12/28/11

ID	Task Name	Duration	Start	Finish	Predecessors
63	**Site Utilities**	**182 days**	**Mon 5/9/11**	**Fri 1/20/12**	
64	Storm Piping/Inlets	4.35 mons	Mon 5/9/11	Fri 9/9/11	13FF+5 wks
65	Water Tap & Distribution	5 wks	Fri 8/5/11	Fri 9/9/11	
66	Finalize Site Lighting Changes	0 days	Wed 9/21/11	Wed 9/21/11	
67	Electric Distribution and Site Lighting	8 wks	Fri 7/1/11	Tue 10/25/11	66FF+5 wks
68	Permanent Power on	0 days	Fri 12/30/11	Fri 12/30/11	
69	Sanitary	4 wks	Mon 9/12/11	Fri 10/7/11	
70	Storm Detention	4 wks	Mon 8/15/11	Mon 9/12/11	
71	Irrigation	4.5 mons	Mon 9/19/11	Fri 1/20/12	
72					
73	**Precast Burial Vaults**	**41 days**	**Fri 7/29/11**	**Mon 9/26/11**	
74	Excavation & Subdrainage System	4.8 wks	Fri 7/29/11	Wed 8/31/11	
75	Crypt Installation	6 wks	Mon 8/8/11	Mon 9/19/11	
76	Backfill	2 wks	Tue 9/13/11	Mon 9/26/11	75FF+1 wk
77					
78	**Exterior Improvements**	**204 days?**	**Mon 6/13/11**	**Mon 3/26/12**	
79	Aluminum Box Culvert	3 days	Tue 9/27/11	Thu 9/29/11	76
80	Retaining Walls	2 wks	Fri 9/30/11	Thu 10/13/11	79
81	Curbs/Walks	12 wks	Mon 8/22/11	Mon 11/14/11	80FF+1 wk
82	Pedestrian Bridge	12.6 wks	Mon 6/13/11	Fri 9/9/11	
83	Site Signage	2 wks	Mon 11/21/11	Fri 12/2/11	
84	Flag Poles	4 wks	Mon 12/12/11	Fri 1/6/12	
85	Site Fine Grading	8 wks	Tue 12/6/11	Mon 1/30/12	43FF,63FF,81FF+
86	Asphalt Paving (base course)	6 wks	Mon 10/31/11	Fri 12/9/11	
87	Memorial for War on Terrorism	45 days?	Mon 12/12/11	Fri 2/10/12	
88	Fountain	30 days?	Mon 12/12/11	Fri 1/20/12	
89	Carillon Tower	65 days	Tue 12/27/11	Mon 3/26/12	
90	Substantial Completion	0 days	Mon 3/26/12	Mon 3/26/12	78,73,63,56,43,30
91	Asphalt Paving (wearing course)	1 wk	Mon 4/9/12	Fri 4/13/12	
92	Final Completion - General Construction	0 days	Mon 4/23/12	Mon 4/23/12	90FS+20 days,91
93	Landscaping	152 days?	Thu 10/20/11	Fri 5/18/12	

BBLCarlton
900 Lee Street, Suite 1400
Charleston, WV 25301
"The Way to Build Today!"
Phone 304.345.1300
Fax 304.345.1304
www.BBLCarlton.com
WV028886

Task	Milestone	Rolled Up Critical Task	Split	Group By Summary
Critical Task	Summary	Rolled Up Milestone	External Tasks	Deadline
Progress	Rolled Up Task	Rolled Up Progress	Project Summary	
